

Work Order ID 149585

Monday, July 25, 2016 2:37:25 PM

149585

Page 1

Item ID: D119-796-251

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 7/26/2016 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/22/2016 Req'd Qty: 1.00 ***1***

Customer:

Reference:

DAS
21Approvals: Process Plan: 9-89 Date: **AUG 02 2016**

Tooling:

Date:

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____

Date:

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
----------	--------------

D119-796-251	D
--------------	---

110

Document Control

0.00

110

DC

Memo

0.00

Doc.Control -USB or Paperwork

Photocopy bluefile and create labels as per PPP D119-796-251 chg 002

DAS
21
9-89

OCT 05 2016

120

Pick Kit
Packaging

0.00

120

Packaging

Memo

0.00

Packaging

130

Crosstubes

0.00

130

Crosstubes

Memo

0.08

Crosstubes

1- Install step and clamp with the proper position per dwg D119-796-251

Torque all clamps to 50 IN-LBS max.

label

1

1

4-10-16

4-10-16

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY			
Environment ☐		No Re-verification ☐		Pressure/Forced ☐		Temperature/Cure ☐	
Design ☐		Operator ☐		Bending ☐		Set-up ☐	
Doc/Data ☐		Offset/Setup ☐		Centre Not Concentric ☐		BOM/Route ☐	
Equip/Tooling ☐		Supplier ☐		Cracks ☐		Broken/Damage/Defect ☐	
Handling/Pre ☐		Training ☐		Crimp/Kink/Ripple/Wave ☐		Inspection Incomplete/Unqualified ☐	
Material ☐		Use for Testing ☐		Cuffs ☐		Contamination ☐	
Internal Transport ☐		Poor Information ☐		Crushing ☐		Countersink ☐	
Tribal Knowledge ☐		Rushing ☐		Heat Treat ☐		Cut Too Short ☐	
LOA ☐		Product Improvement ☐		Wave/Twist in Tube ☐		Instructions Incomplete/Unclear ☐	
Substation ☐		Process Improvement ☐		Marks/Chatter ☐		Drill Holes ☐	
Past Expiry Date ☐		Manufacturing Process ☐		OTHER : _____			
Misidentified ☐		Past Due ☐					

Work Order ID 149585

Monday, July 25, 2016 2:37:25 PM

149585

Page 2

Item ID: D119-796-251

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 7/26/2016 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 8/22/2016 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140	QC5- Inspect part completeness to step on W/O	0.00							
140									
QC									
Quality Control									
	Memo	0.00							
	RE-CHECK TORQUE ON CLAMP AS PER DWG.								
	***VERIFY BY <u>149585</u> <u>DAS</u> <u>9-89</u> BATCH # TO MATCH W/O								
	***VERIFY BY <u>149585</u> <u>DAS</u> <u>9-89</u> PART # TO MATCH								
	W/O <u>149585</u> <u>DAS</u> <u>9-89</u>								
150		0.00							
150									
Packaging									
Packaging									
Packaging									
	Memo	0.00							
	Identify and pack for shipping as per PPP D119-796-251								
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC									
Quality Control									
	Memo	0.02							

DAS
21
9-89

OCT 05 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER :			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Monday, July 25, 2016 2:37:24 PM

Page 1

Work Order ID: 149585

149585

Parent Item: D119-796-251

D119-796-251

Parent Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 7/26/2016

Required Date: 8/22/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 14.09.09 NEW ISSUE DD VERF:JLM IPP REV:B
14.10.15 AS PER REV.A DD VERF:JLM IPP REV:C 14.11.19
AS PER REV.C DD VERF:JLM IPP REV:D 14.12.09 AS PER
REV.PC6 DD VERF:JLM IPP REV:E 15.02.11 AS PER REV D
JLM VERF:DD

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D119-796-241		Manufactured	No				Each	1.0000		1			
D119-796-241									**				
AFT Crosstube Installation without Step (no hardware)													
				<u>Location</u>				<u>Loc Qty</u>	<u>Loc Code</u>				
				FG				1					
					146580			1					
D5123-3		Manufactured	No				Each	108.0000		4			
D5123-3									**				
Clamp Cushion													
				<u>Location</u>				<u>Loc Qty</u>	<u>Loc Code</u>				
				LG054				12					
					147939			12					
				LG055				96					
					145851			36					
					146879			36					
					148184			24		4			
D5149-043		Manufactured	No				Each	0.0000		2			
D5149-043									**				
Aft Step Base Assembly													

146877

2

4-10-16

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

Picklist Print

Monday, July 25, 2016 2:37:24 PM

Page 2

Work Order ID: 149585

149585

Parent Item: D119-796-251

D119-796-251

Parent Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 7/26/2016

Required Date: 8/22/2016

Start Qty: 1.00

Required Qty: 1.00

MS21920-25

Purchased

No

Each

21.0000

4

MS21920-25

Clamp



21-09-16

Location

Loc Qty

Loc Code

FG

2

120920

2

LG050

19

m134987

19

135538 ~~135538~~

4

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE




QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					


ITEM	QTY	P/N	DESCRIPTION
	X	D119-796-251	XTUBE ASSY (AW119 MKII AFT)
1	1	D119-796-241	XTUBE ASSY (AW119 MKII AFT)
2	4	D5123-3	CUSHION
3	2	D5149-043	AFT STEP ASSY
4	4	MS21920-25	CLAMP

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 149585 MJ
1608-02

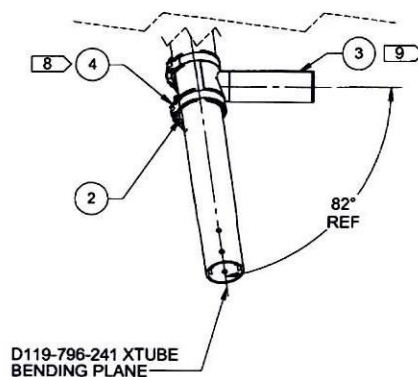

D119-796-241 XTUBE
BENDING PLANE

SECTION A-A

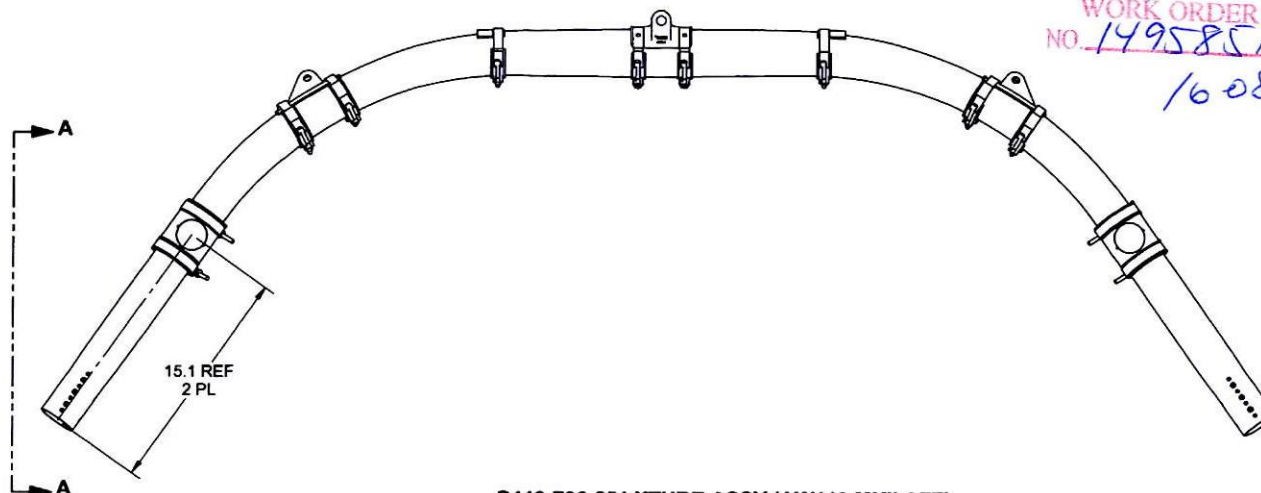

D119-796-251 XTUBE ASSY (AW119 MKII AFT)

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 METHOD 6.5
- 7) WEIGHT: 29.9 lbs
- 8) TORQUE MS21920-25 CLAMPS TO 50 IN-LBS MAX
- 9) LOCATE STEP USING POST FITTING ON CROSSTUBE

RELEASED

2015 FEB 09

ECN 15-516

D	D5123-3 WAS D5123-9, MS21920-25 WAS -26, ADDED SECTION A-A	AP	15.01.19
C	RE-DESIGN STEP INSTALLATION	DB	14.11.24
B	D2274 RADIUS BLOCK WAS D5153-1, AN4C12A WAS AN4C10A	AP	14.10.04
A	NEW ISSUE	AP	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D119-796-251	SHEET 1 OF 1
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	XTUBE ASSY (AW119 MKII AFT)	NTS
DATE	15.01.19	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

APPROVED
